

# Rye Park Wind Farm Construction Update



**Week commencing 27 June 2022 - look out for the June newsletter in the mail this week**

*Construction Updates are released fortnightly and include a summary of construction works undertaken and a look-ahead of upcoming works.*

The Tilt Renewables team and construction contractor Zenviron (and their subcontractors) are continuing with building the 396 MW Rye Park Wind Farm project including main access track to northern and southern substation benches. Internal civil works also continue inside the three site entry points including hardstand and foundation construction. The ARDG quarries will continue supplying gravel to cap the internal access tracks, compound laydowns and batch plant benches (similar to a hardstand for stockpiling materials). The northern batch plant has been commissioned and will commence delivering concrete for foundation blindings (base layer of concrete) between the two northern site entries.

**Road users should still expect minor delays and diversions while the road works are being undertaken along Grassy Creek Rd, Yass St, Dalton Rd, Boorowa bypass and Boorowa-Rye Park Rd. If travelling along these routes, please be mindful of the works and follow traffic control directives and enforceable road work speed limits.**

**Grassy Creek Road Works:** Works on Grassy Creek Rd continue with the Pudman Creek bridge upgrade progressing slowly due to inclement conditions. Installation of roadside drainage continues with culverts and erosion protection. Grassy Creek causeway bypass removal and remediation works continue. Installation of road furniture is complete. Reinstatement of landowner access points will continue in this reporting period.

**Boorowa Road Works:** Rehabilitation works to continue through Boorowa with road furniture and line marking continuing along Boorowa/Rye Park Rd, with anticipation of works finishing in this reporting period. Ongoing maintenance will also continue along Boorowa/Rye Park Rd.

**Dalton Road:** The upgrade of Dalton Rd South off the main project entry continues including ripping, recompacting and gravel placement. It is anticipated that the two-coat seal will start week commencing 27 June. Flakney Creek causeway and drainage is completed with the two-coat seal of the approaches scheduled for 27 June. Due to the frequency of heavy vehicles and the high levels of wet weather, further areas have degraded along Dalton Rd. These areas will be repaired with ongoing maintenance expected for the duration of the Project.

*...continued on page 2.*

**If you have any questions or concerns, please contact:**  
**Tilt Renewables - Site HSEC Manager: Andrew Galland - 0447 076 886, or**  
**Zenviron - Site Manager: Sasa Stegic - 0499 011 861**



For any questions or feedback, please get in touch by calling: **1800 WE TILT** (938 458)

Email: [ryeparkwindfarm@tiltrenewables.com](mailto:ryeparkwindfarm@tiltrenewables.com) | Web: [www.ryeparkwf.com.au](http://www.ryeparkwf.com.au)

Postal Address: PO Box 16080 Collins St West, Melbourne Vic 8007

**Sign up for updates by subscribing to the newsletter and construction updates via SMS**

Use the QR code provided to sign up or contact us on 1800 WE TILT and we'll do it for you.

You can text us too. Text +61 480 096 779 if you have any questions and we'll give you a call back.

# Rye Park Wind Farm Construction Update




**Week commencing 27 June 2022**

*Construction Updates are released fortnightly and include a summary of construction works undertaken and a look-ahead of upcoming works.*

**Cooks Hill Road:** Tilt Renewables continues to work with Upper Lachlan Shire Council to finalise the design of the Cooks Hill Road upgrade. The final design is being developed to address key biodiversity and heritage constraints, whilst balancing road safety considerations. Both parties are working as a priority to finalise the design and undertake works as soon as practicable. Until such time the works are completed, the Project will continue to maintain the road.

**Yass St, Rye Park:** Works along Yass St (Rye Park village) continue to progress with causeway works and approaches to be bitumen sealed in the coming period. Yass St footpath rehabilitation continues along with the continuation of Yass St driveway tie-ins. *Progress photos included below.*

**The Outpost food van stationed at the Rye Park Rec Grounds is well into operations, continuing to sell coffee and food from 7am to 2pm.**

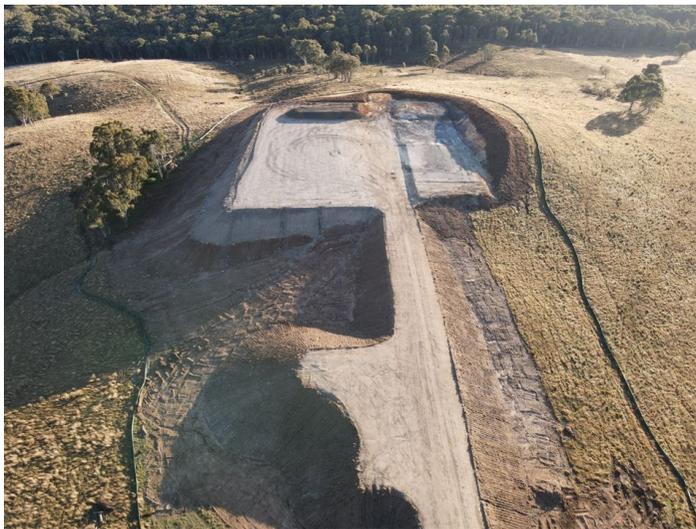

*Left to right: Wind turbine hardstand complete, concrete batching plant and bench, The Outpost Food Van in the Rye Park village.*

For any questions or feedback, please get in touch by calling: **1800 WE TILT** (938 458)

Email: [ryeparkwindfarm@tiltrenewables.com](mailto:ryeparkwindfarm@tiltrenewables.com) | Web: [www.ryeparkwf.com.au](http://www.ryeparkwf.com.au)

Postal Address: PO Box 16080 Collins St West, Melbourne Vic 8007

**Sign up for updates by subscribing to the newsletter and construction updates via SMS**

Use the QR code provided to sign up or contact us on 1800 WE TILT and we'll do it for you.

You can text us too. Text +61 480 096 779 if you have any questions and we'll give you a call back.
